

FOCUS ON: BLACKHEAD COASTAL PATH



projectupdate

Upper path works are substantially complete, with the remaining portion to be completed after the promenade works. The handrail has been installed on the steps, as well as fencing and an area of erosion control blanket. The access from the car park to the upper path has been washed in preparation for the surface treatment. An old culvert at the northern end of the rock armour revetment has been renewed with a precast concrete pipe and headwall with a rock surround. The rock revetment works are progressing well with 130m of rock armour revetment now completed with the remaining toe stone placement due to commence in the coming week. Works on the lower revetment has also been taking place. Preparation for the works on the concrete promenade are currently underway with excavation of the current structure due to commence next week. A geological survey was undertaken using rope access to review the current condition of the cliff face along with the proposed design of the repairs (mesh, scaling, bolting).

Picture: Aerial view of the ongoing work on the Blackhead Coastal Path

upcomingworks

Deliver and stockpiling stone
Now until end of September 2019

Rock Armour Revetment Works
Now until Autumn 2019

Concrete Promenade works
Now until December 2019

Upper path (Section A)
Works will be completed after promenade works

Cliff Face Repairs
Commences October 2019


Pathworks (Section B)
Commences October 2019



FOCUS ON: BLACKHEAD COASTAL PATH



40 tonne dumper delivering rock armour stone

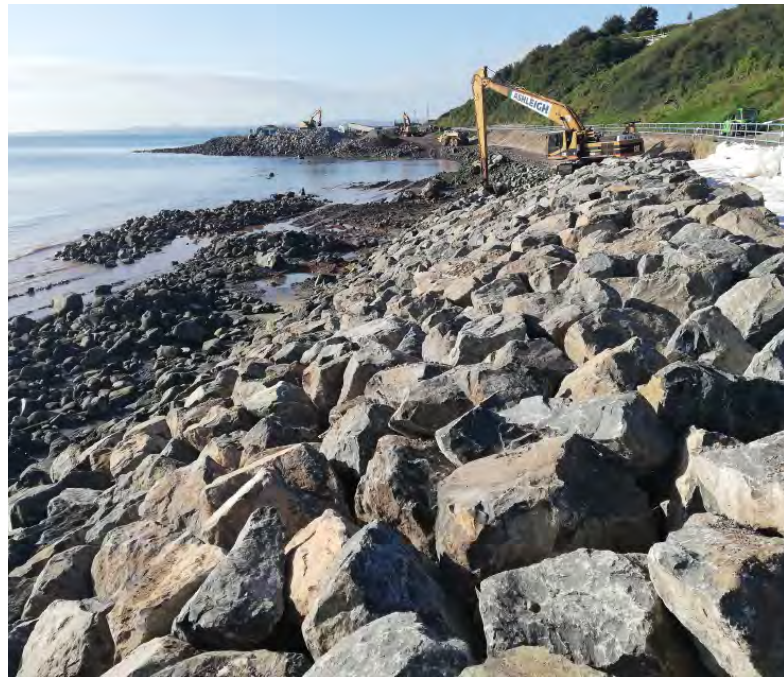

Rock armour revetment



Common lizard sunbathing on some ply alongside the promenade



Culvert has been renewed with FP McCann Precast concrete headwall and pipes



Geological Survey

contactdetails

Site Office:

Blackhead Path Car Park, Old Castle Road, Whitehead
T: 028 2563 3508 / bhp@fpmccann.co.uk

For FP McCann:

Rebecca Henderson (Liaison Officer)

For MEABC:

Colin Morrison (Project Development Officer)

FP MCCANN LEADING THE WAY IN REVETMENT WORKS

